



expert in
sports hall
development

POOLE GRAMMAR SCHOOL

PROJECT OVERVIEW

"Planning for a new school sports hall can be a long process. For Poole Grammar this has taken 10 years from our initial plans to the delivery of a wonderful facility for our school and local community. Alastair and Alan from Ball Hall have stuck with us throughout this period and helped us realise our dreams despite the pressures facing the construction industry and school funding. We would recommend Ball Hall to others who are considering new sports halls."

JONATHAN STIBY, POOLE GRAMMAR SCHOOL



expert in
sports hall
development

POOLE GRAMMAR SCHOOL

Five badminton court size hall with indoor cricket nets, basketball, netball, badminton, volleyball, futsal and handball provision.

COST

£4m

excl VAT

LOCATION

Poole

Dorset

OPENED

Sept 2023



FACILITIES AT POOLE GRAMMAR SCHOOL



SPORTS EQUIPMENT



GYM



SPORTS FLOORING



CHANGING ROOMS
& TOILETS



OFFICES &
MEETING ROOMS



ACCESSIBILITY



CLASSROOMS





expert in
sports hall
development

PROJECT CHALLENGES

Funding


Being a state school, there were not many funding agencies prepared to fund the project. The school applied for CIF funding because their existing sports hall was condemned based on its condition and fitness for purpose.

Asbestos

There was a significant amount of asbestos found when an intrusive demolition and refurbishment survey was undertaken. The asbestos was in an unusual location between the ceiling and roof and was of a type that required the most careful removal. It meant a birdcage scaffold enclosed with polythene over the whole roof with negative pressure ventilation and the existing roof dismantled bit by bit during the very hot summer of 2022. The asbestos caused an abnormal programme impact and financial impact on the project.

Access and Safety

The only access meant driving through the school entrance, across a school playground and down a fire path in the occupied school.

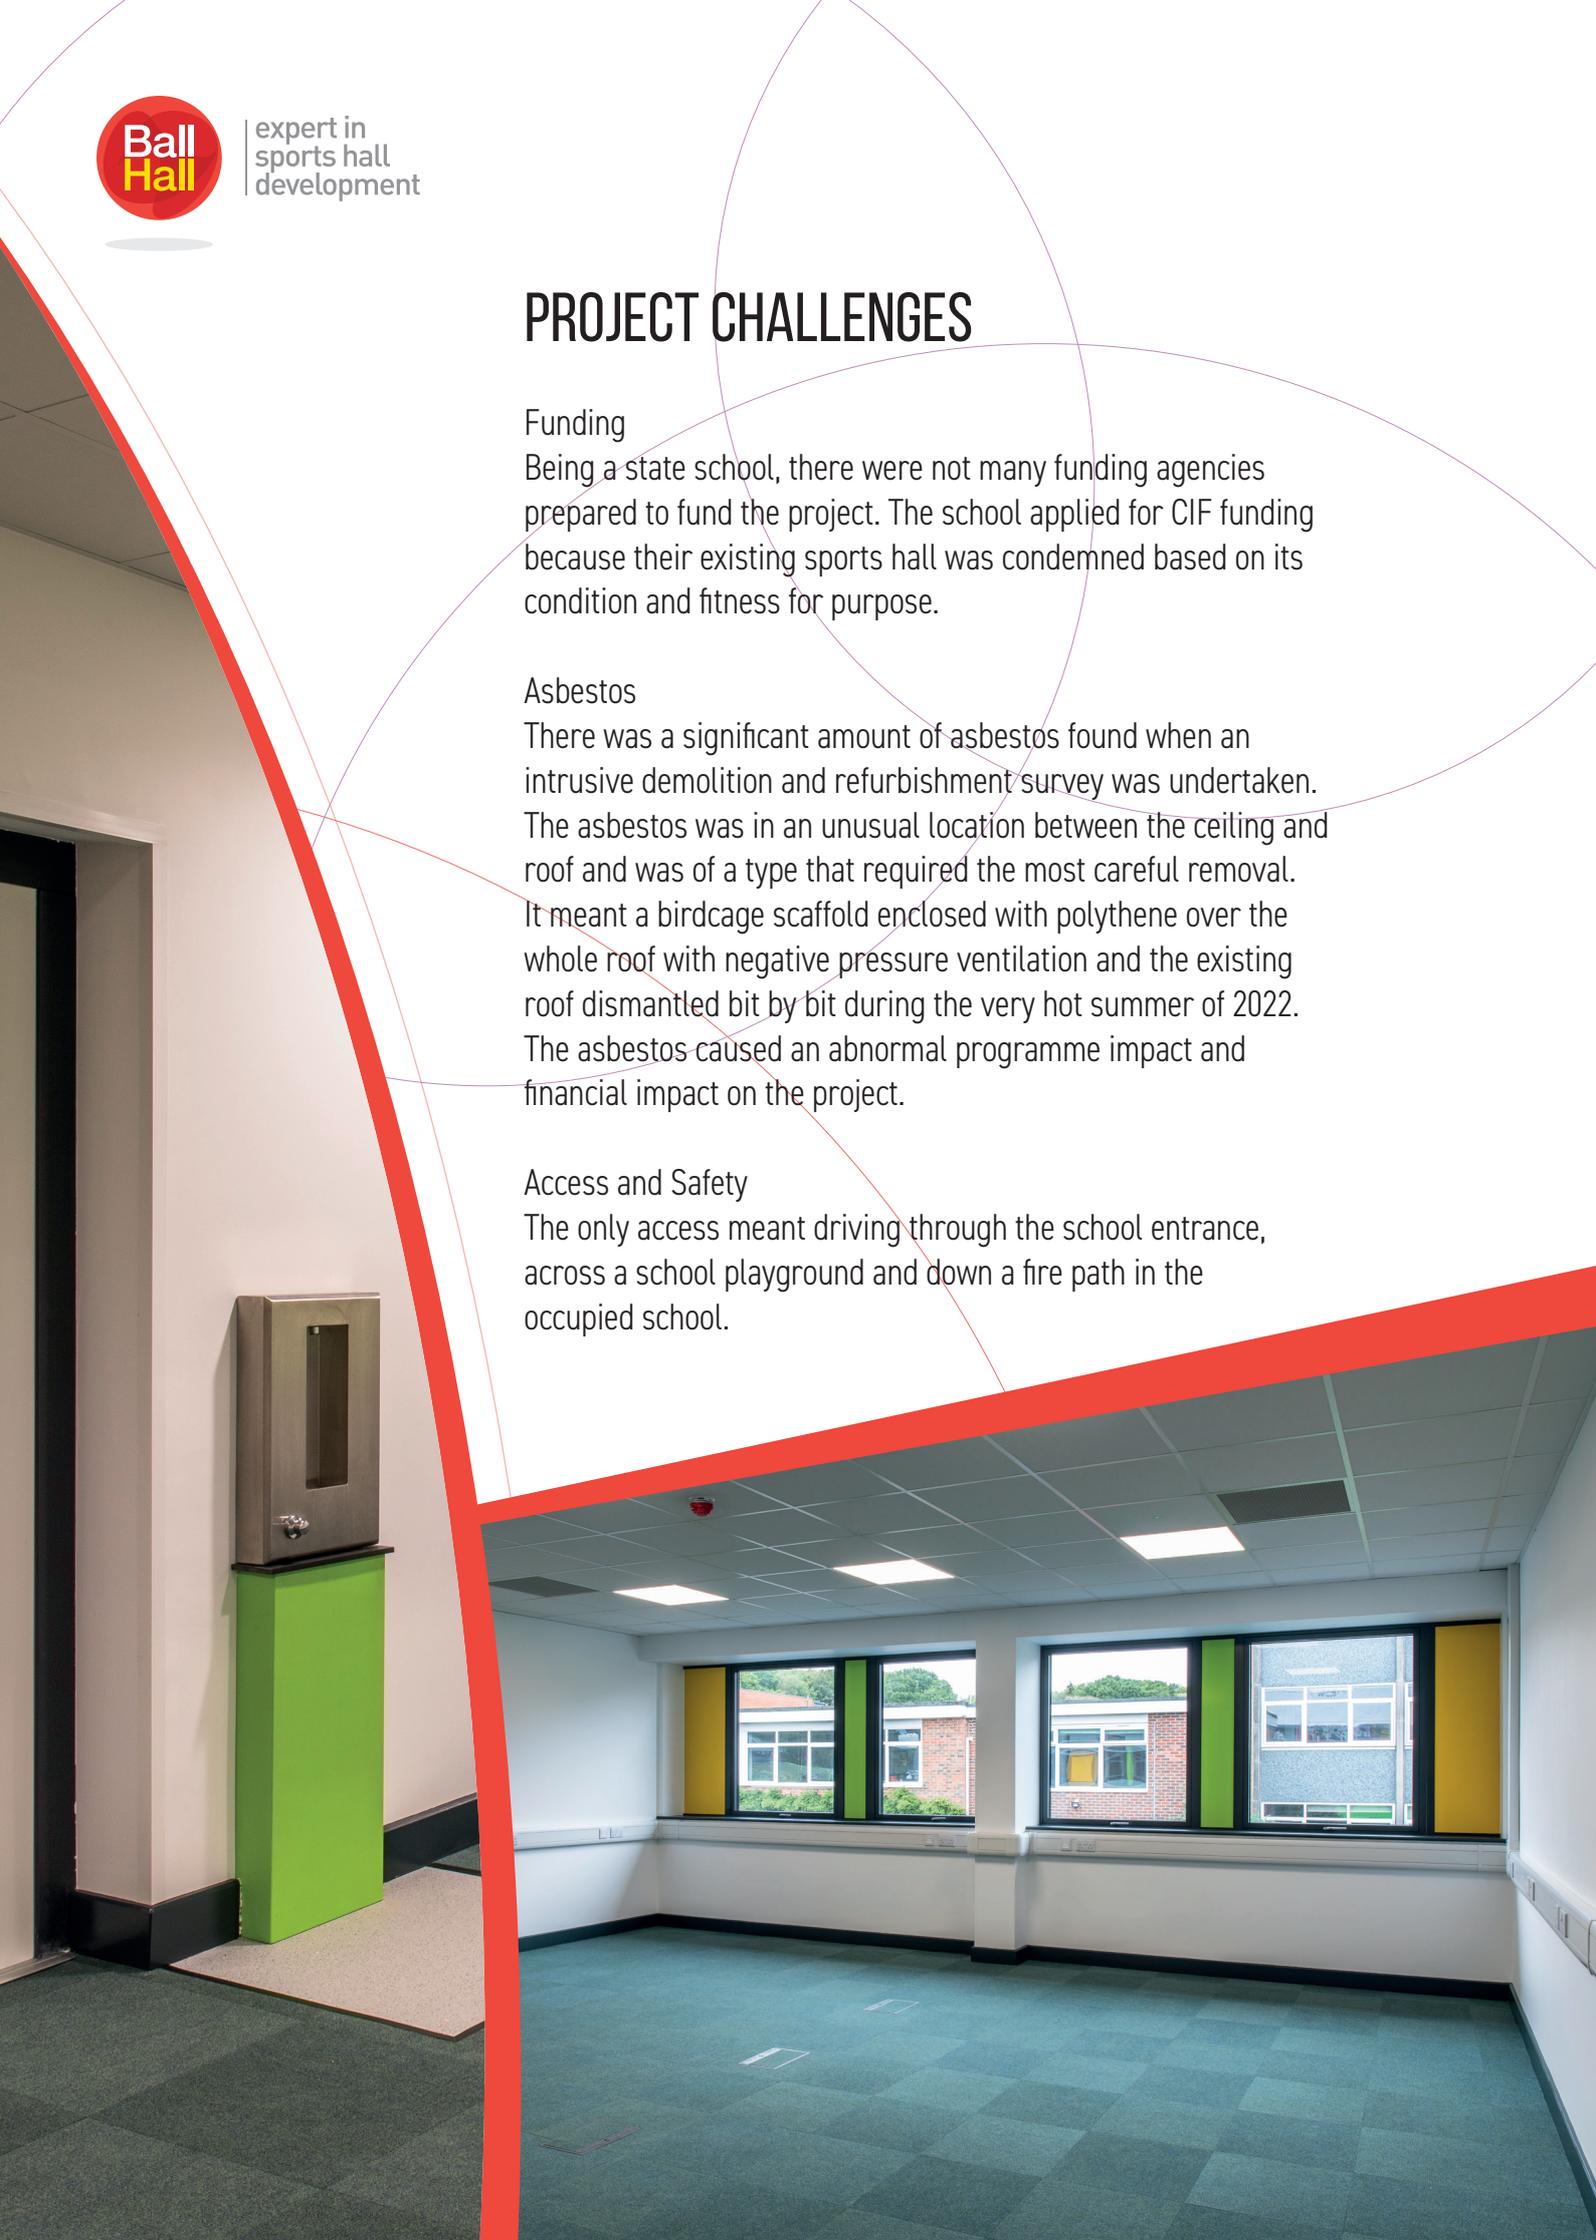



expert in
sports hall
development

PROJECT SOLUTION

Funding


We helped the school build the case for the CIF funding based on their need. We produced the floor layouts, a Cost Plan and a risk management strategy to convince the ESFA that the project was robust and financially sound.

Asbestos

We programmed the works carefully so the asbestos removal would take place in the summer holiday of 2022 and to still allow completion of the building ready for the new school year in September 2023. The financial impact of the asbestos discovery meant that we had to adopt a value engineering exercise, which we were able to do successfully without compromising on any of the key requirements of the school.

Access and Safety

We liaised carefully with the school to ascertain the best route for traffic. Setting out vehicle and pupil movements with systems in place including level crossing type arrangement gates that meant no vehicles could cross areas at the same time as pupils. Enforcing a requirement that all vehicles were walked into the site with a banksman and prohibiting any deliveries during the busy school drop off and pick up times.

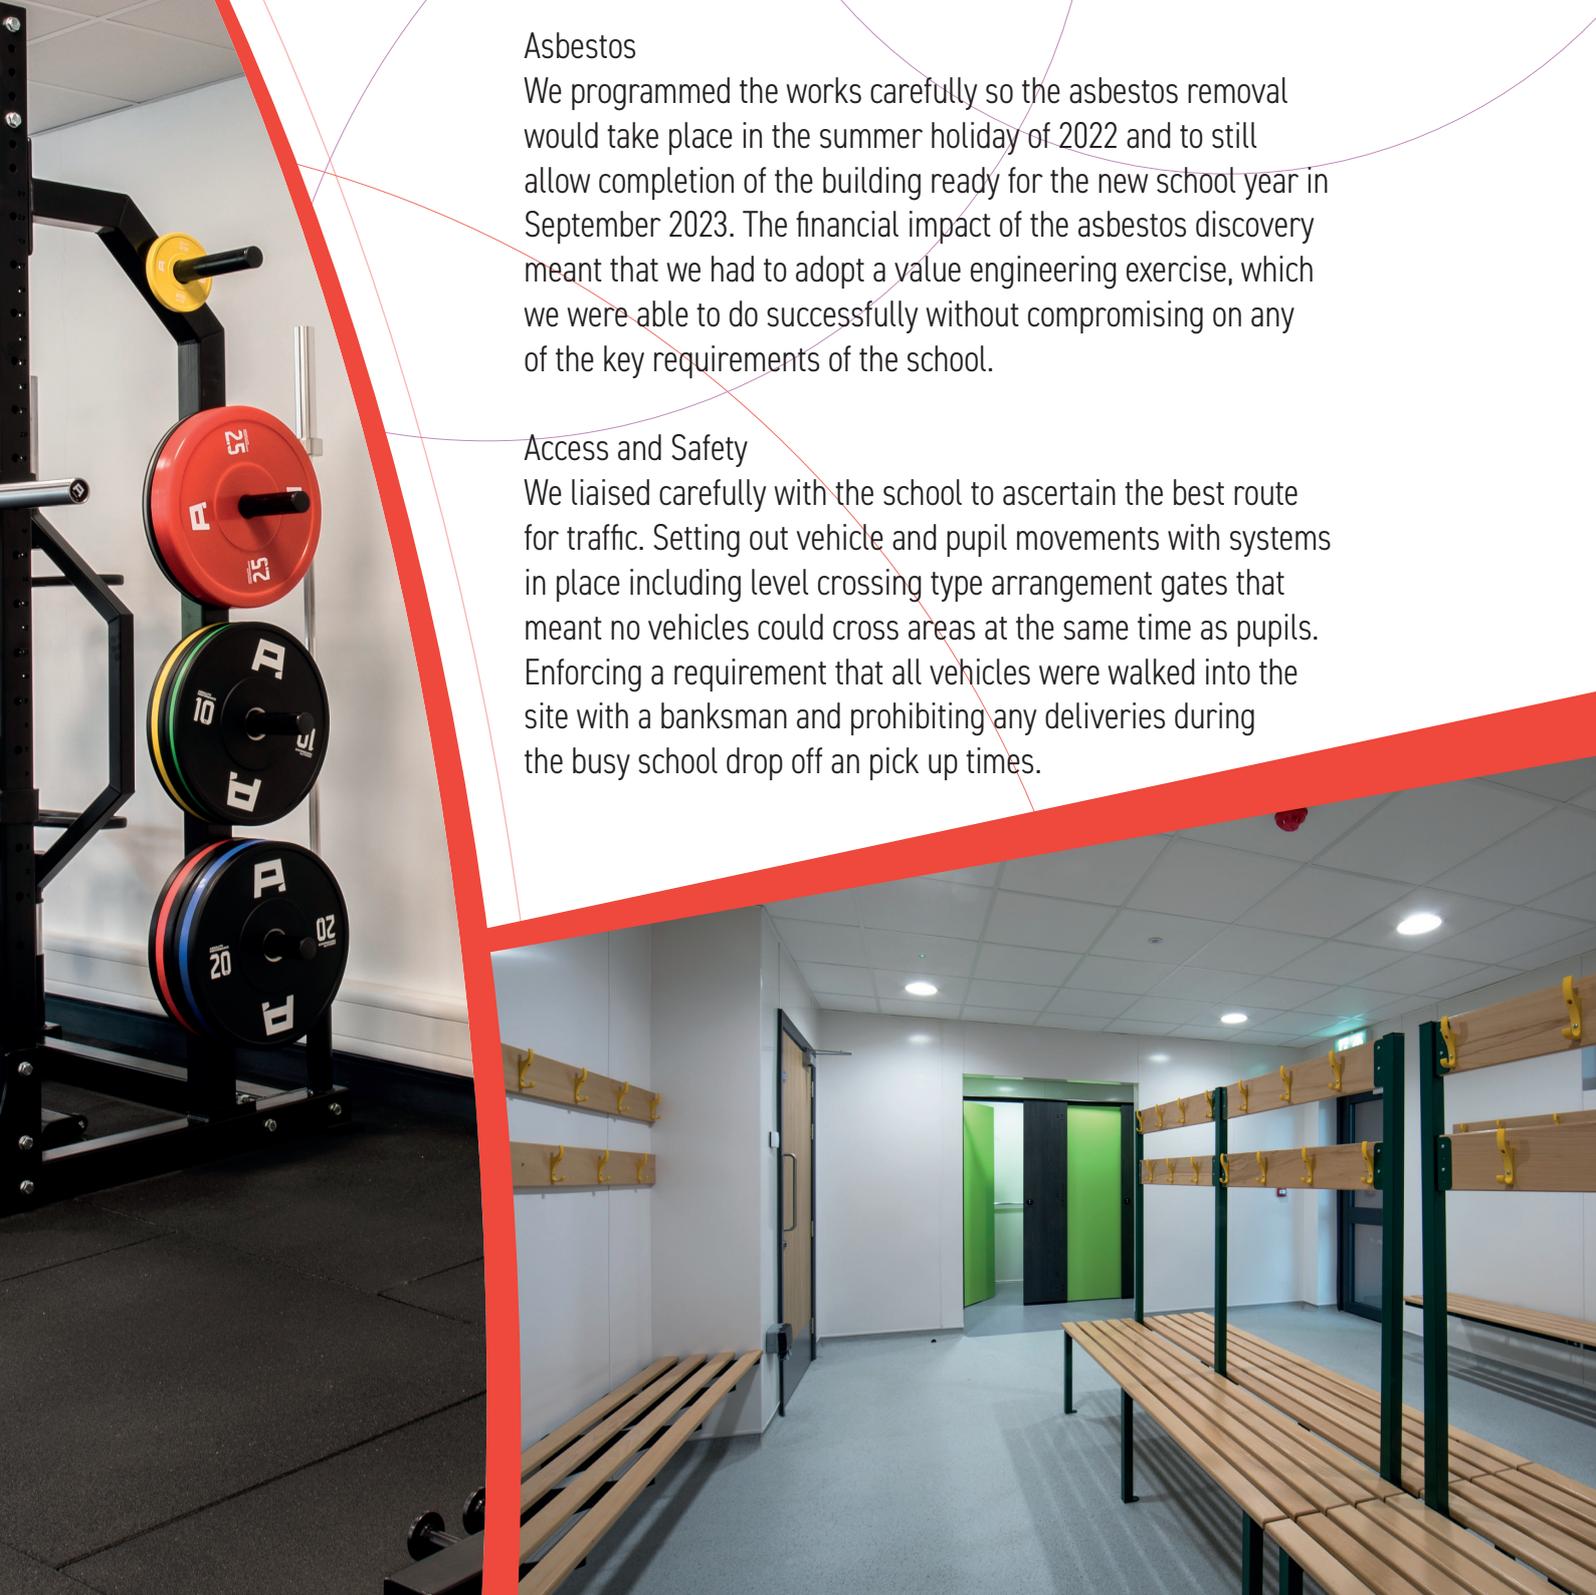



expert in
sports hall
development


BALL HALL ADDED VALUE

We worked with the school for many years helping them build the case for the new sports hall. We provided information directly for the ESFA and in response to queries from the DfE. Knowing the school did not have the funding for the building in these early days, we carried out a lot of our initial services at risk.

The school hadn't previously overseen large building projects, so we guided them through the whole process and took away any concern they may otherwise have had by administering the project proactively and diligently.

Our knowledge of health and safety and working in schools helped formulate a plan for the construction works whilst keeping disruption to the school to an absolute minimum.



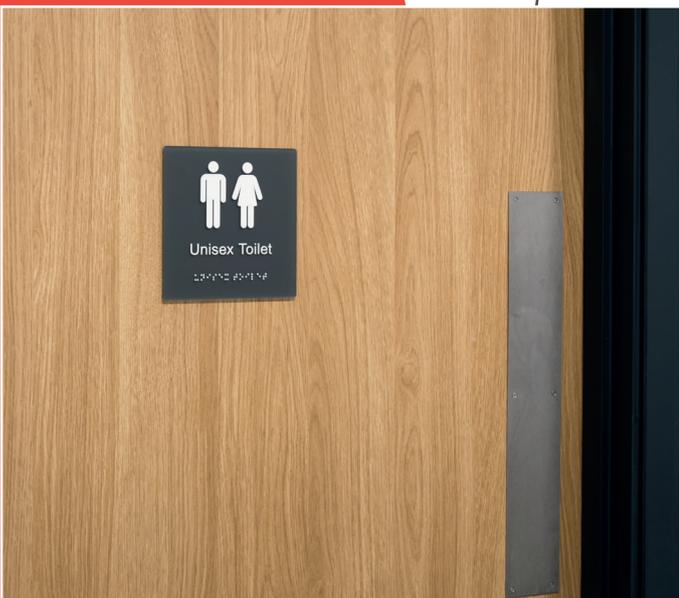

01664 567 542
info@ballhall.co.uk
ballhall.co.uk



expert in
sports hall
development
